



Odcinek A Eurovia

	26.03	2.04	10.04	16.04	23.04	30.04	7.05	14.05	21.5
warstwa ścierna	0%	0%	0%	0%	0%	0%	0%	3%	13%
warstwa wiążąca	43%	43%	43%	44%	53%	69%	76%	97%	99%
warstwa podbudowy	83%	88%	89%	89%	92%	95%	95%	100%	100%

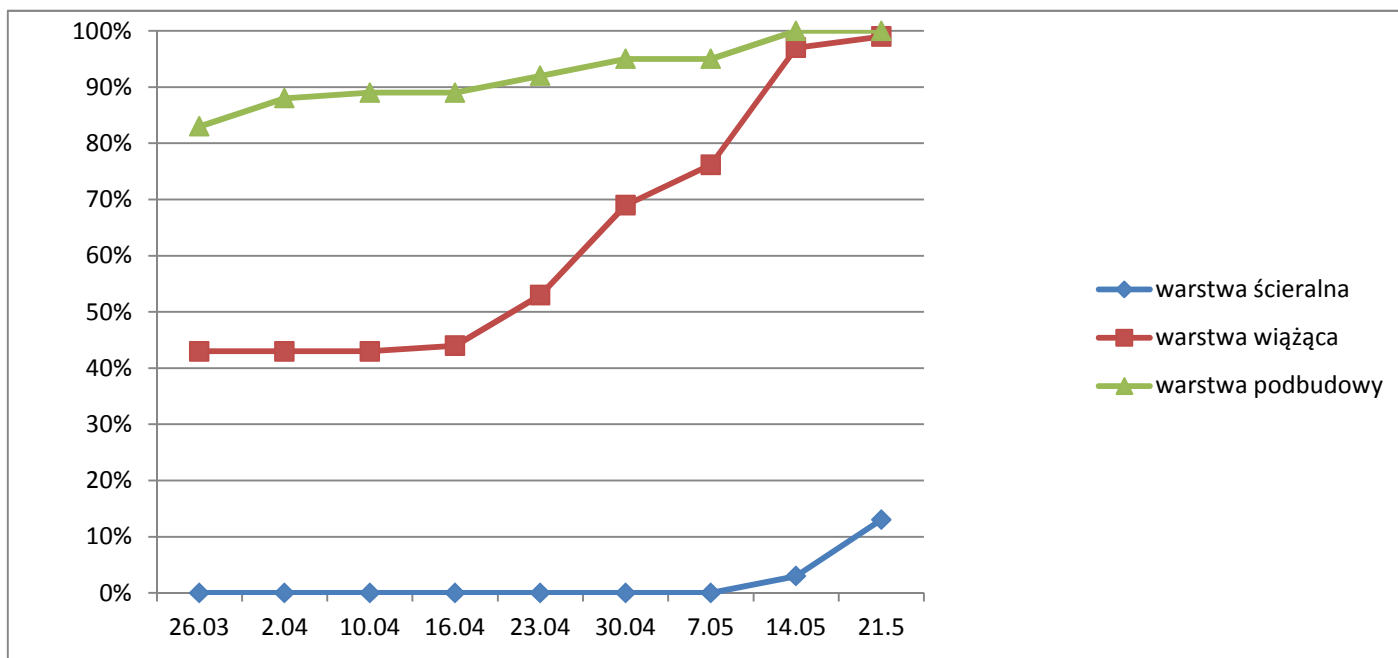


Odcinek B Mostostal

	26.03	2.04	10.04	16.04	23.04	30.04	7.05	14.05	21.05
warstwa ścierna	0%	0%	0%	0%	5%	30%	51%	81%	98%
warstwa wiążąca	41%	42%	43%	67%	81%	90%	100%	100%	100%
warstwa podbudowy	89%	90%	95%	96%	97%	99%	100%	100%	100%

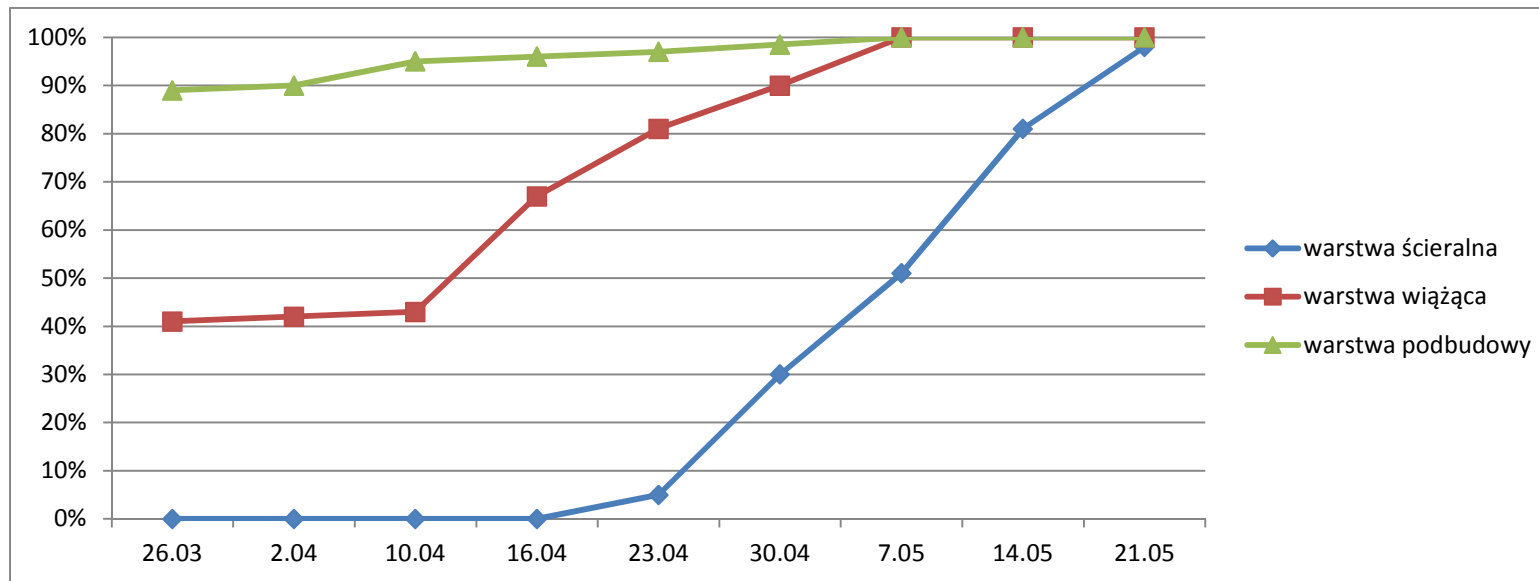


Odcinek C Boegl&Krysl

	26.03	2.04	10.04	16.04	23.04	30.04	7.05	14.05	21.05
warstwa ścierna	0%	0%	0%	0%	0%	0%	0%	0%	0%
warstwa wiążąca	19%	20%	37%	38%	45%	49%	57%	80%	87%
warstwa podbudowy	39%	41%	46%	53%	53%	62%	73%	81%	94%

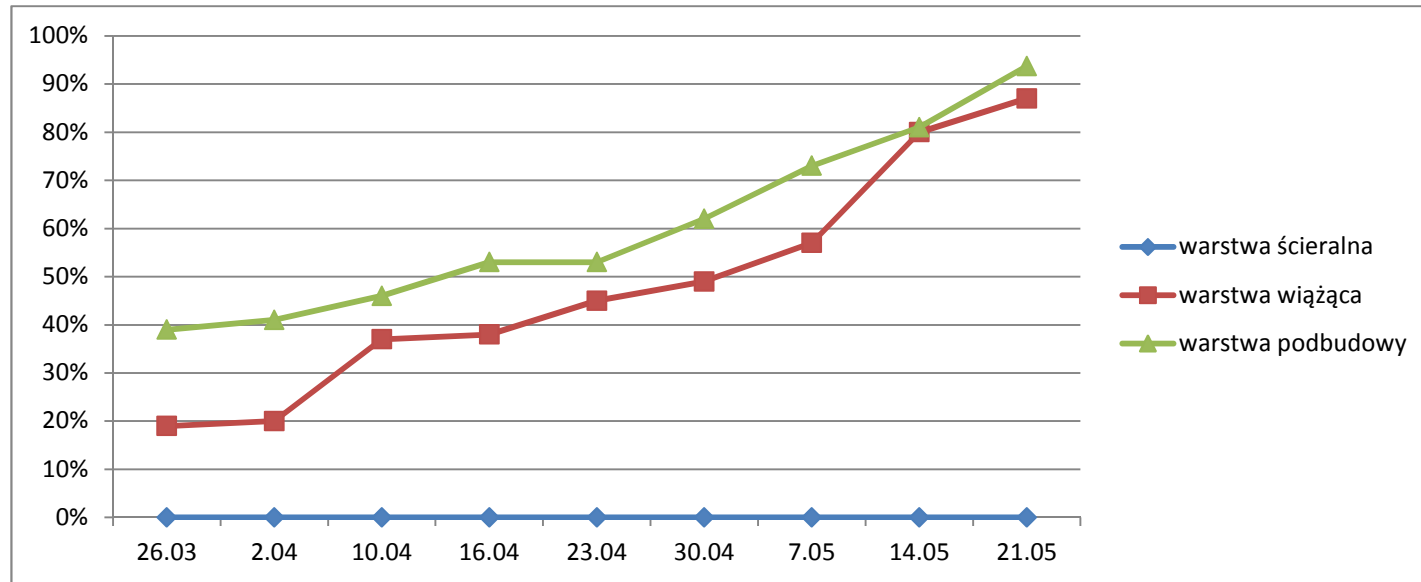

Odcinek D Strabag

	26.03	2.04	10.04	16.04	23.04	30.04	7.05	14.05	21.05
warstwa ścierna	0%	0%	0%	0%	0%	25%	48%	86%	100%
warstwa wiążąca	88%	94%	94%	96%	98%	100%	100%	100%	100%
warstwa podbudowy	93%	94%	94%	98%	99%	100%	100%	100%	100%

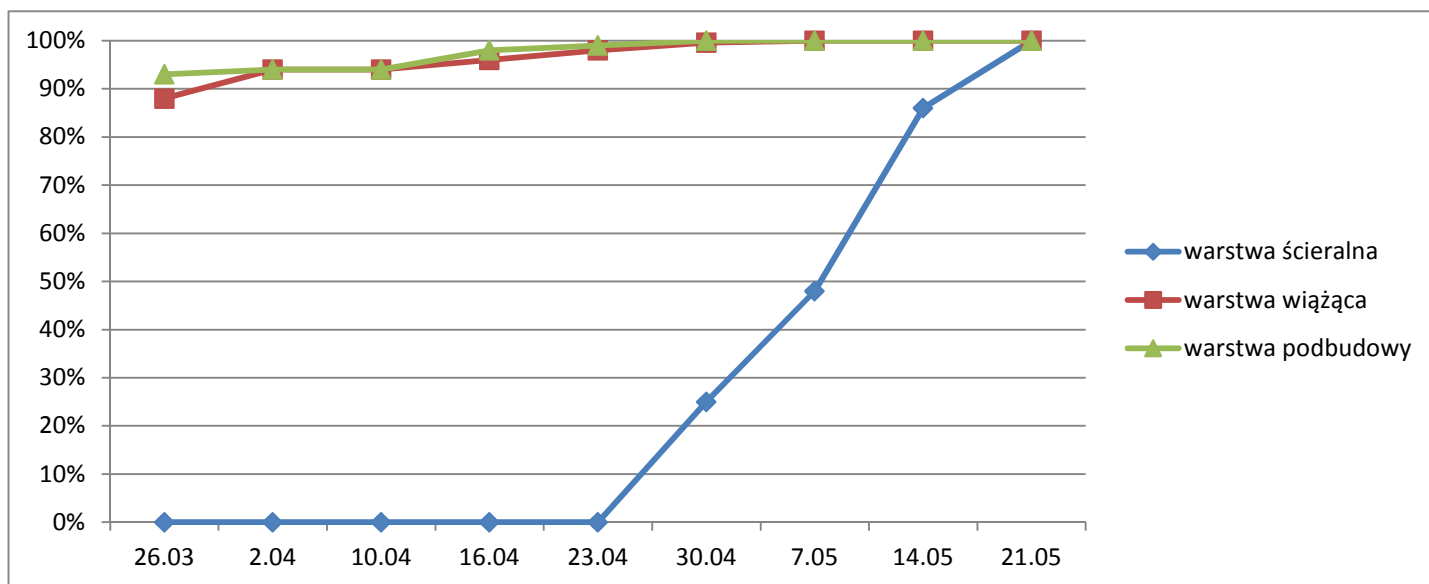

Odcinek E Budimex

	26.03	2.04	10.04	16.04	23.04	30.04	7.05	14.05	21.05
warstwa ścierna	9%	22%	22%	34%	34%	77%	100%	100%	100%
warstwa wiążąca	100%	100%	100%	100%	100%	100%	100%	100%	100%
warstwa podbudowy	100%	100%	100%	100%	100%	100%	100%	100%	100%

